



Saint Paul
PUBLIC SCHOOLS

Highland Park Middle School - Renovation: January 2024 Project Update



Location: 975 S Snelling Ave., Saint Paul, MN 55116

Grades: 6-8

Enrollment (SY22-23): 805

Project website: spps.org/Page/46814

School website: spps.org/highlandms

Project summary

Project number: 3081-23-01

Funding: Certificates of Participation, Long Term Facilities Maintenance

Project type: Addition and renovation

Square footage:

- Existing: 168,968 SF
- Proposed: 19,560 SF

SPPS project team:

- Mike Christen, Project Manager
- Jhalil Payne, Project Coordinator

Design team: ATS&R

Construction team: Kraus-Anderson Construction

Project scope

- New identifiable front entrance and main office
- Two-story link addition
- Fully-remodeled kitchen and cafeteria
- Renovated special education suite
- Updated classroom technology
- Gym floor replacement; substantial renovations of existing spaces
- Inclusive restrooms
- Replacement of sidewalks, ramps and landings; updates to parking lot with new parent drop-off lane
- Stormwater management and landscaping

New this month

- Project is officially advertised with contractor bids being due December 19; contracts over the \$175K threshold will be presented to the Board of Education for approval on January 23, 2024.


January 2024 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete (as invoiced)
\$49,500,000	\$3,876,678	\$701,977	TBD	\$0	0%	\$49,500,000	0%

Project Timeline

Phase: <i>Planning</i> → <i>Design</i> → <i>Construction</i> →							
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award			Closeout
Key dates:	✓ March 2021	✓ Sept. 2022	✓ July 2023	☐ TBD			☐ Fall 2025

Highland Park Middle School

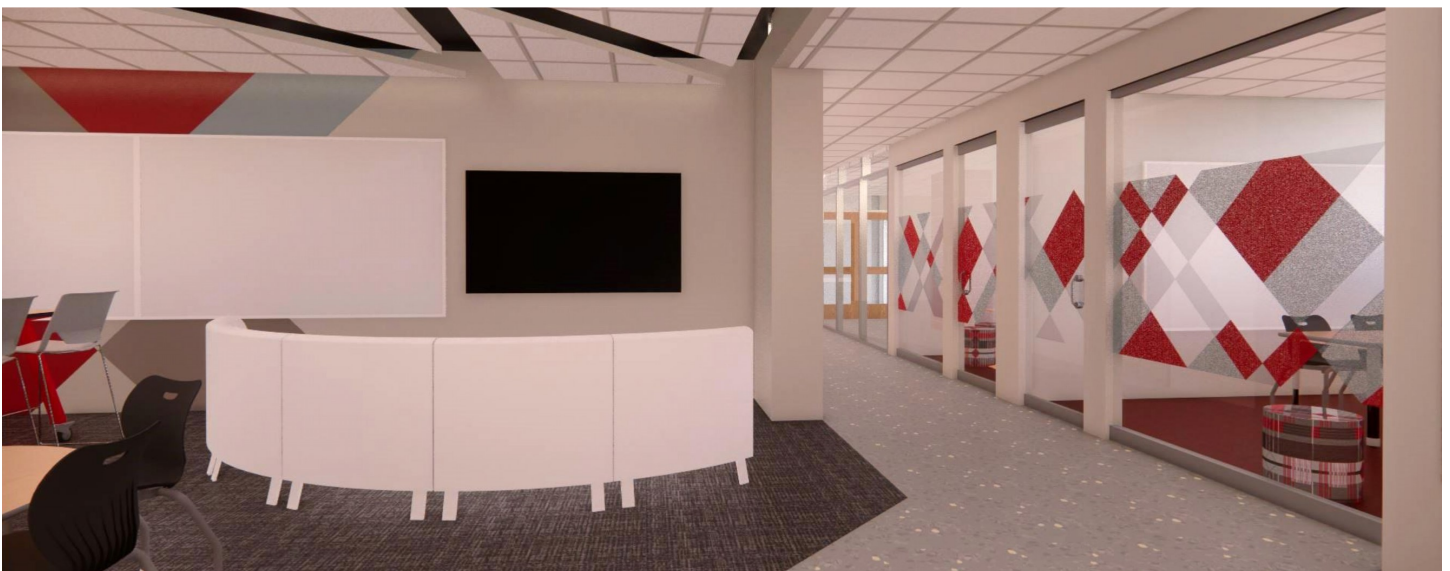

From top: Renderings of reception area, breakout and small-group rooms, and cafeteria
